

McCownGordon Construction

PROJECT MONTHLY UPDATE

Sunflower Fire Station

08/30/24

SUMMARY

This is a monthly construction update that is designed to keep everyone informed of the current Project status. Please feel free to reach out with any questions.

Project rendering sign at 102nd and Lexington



CONFIDENTIAL WORK PRODUCT – COPYRIGHT 2024 | McCownGordon Construction, LLC, All Rights Reserved

McCownGordon
CONSTRUCTION



Fire Station Pad ready for footings



McCownGordon mobilized to site



CONFIDENTIAL WORK PRODUCT – COPYRIGHT 2024 | McCownGordon Construction, LLC, All Rights Reserved

McCOWNGORDON
CONSTRUCTION



George J Shaw mobilized to site



CONFIDENTIAL WORK PRODUCT – COPYRIGHT 2024 | McCownGordon Construction, LLC, All Rights Reserved

McCOWNGORDON
CONSTRUCTION



Thrust blocks at fire line and domestic line were installed



CONFIDENTIAL WORK PRODUCT – COPYRIGHT 2024 | McCownGordon Construction, LLC, All Rights Reserved

McCOWNGORDON
CONSTRUCTION



First footing dig at NE corner of building pad in app bay



South footing at living quarters were poured




CONFIDENTIAL WORK PRODUCT – COPYRIGHT 2024 | McCownGordon Construction, LLC, All Rights Reserved

McCOWNGORDON
CONSTRUCTION



Drone photo of footing progress as of 8/19/25

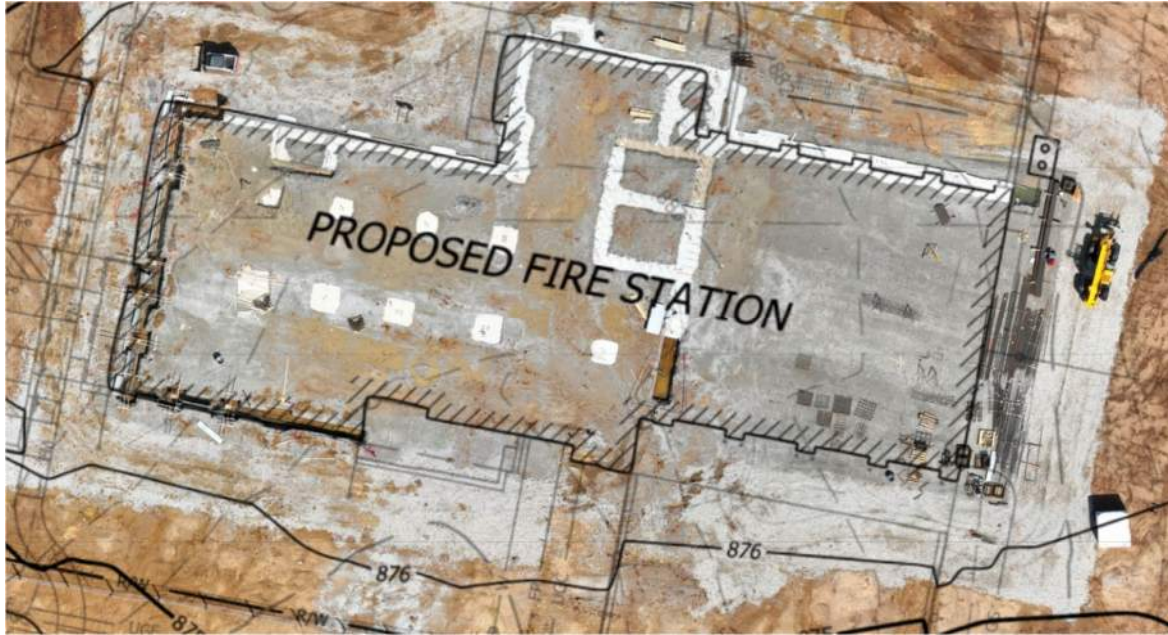

Weather Days this month:

- 6 weather days for the month of August.

Activities planned for the next month:

- Remobilize on 102nd Street rock removal for road
- Complete footing activities
- Under slab plumbing and electrical rough-in
- CMU first course at all CU wall locations
- Edge forms at perimeter of living quarters
- Under slab drainage course
- Under slab vapor barrier and reinforcement

-The McCownGordon Team
